
PAVING THE WAY: EXPLORE THE NEW

CBR TRAIL

CBR Trail construction is ongoing in the Town of Addison. The following is an update of construction work performed during the month of September 2026.





TOWN OF **ADDISON**

COTTON BELT REGIONAL TRAIL *(CBR TRAIL)*


CONSTRUCTION STATUS NEWSLETTER

PROGRESS PHOTOS
See photos of the trail constuction:
https://tinyurl.com/CBRT-Addison-Sept2026

MONTHLY UPDATES
Stay tuned for upcoming monthly newsletters!

CONTACT US!
Reach out to the project team with questions at:
(214) 585-7308

ACTIVITY
Stay posted with updates by roadway *below!*

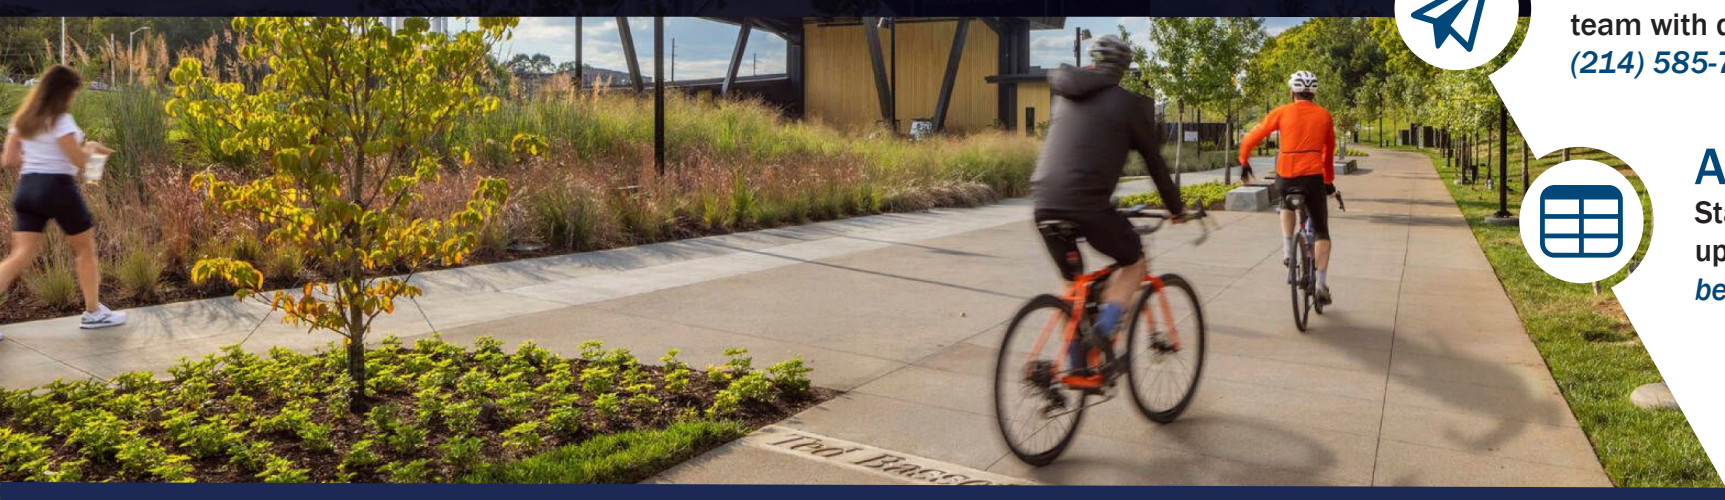

CONSTRUCTION UPDATE MAP

LEGEND
- TRAIL IN PROGRESS
- TRAIL COMPLETE
- PHASE 3A: MARSH LN. TO MIDWAY BRIDGE

ADDISON (1.1 MILES)
WORK DATES: 05/14/25 - 03/14/27
TOTAL FEET (TF): 5,808 TF
TF INSTALLED: ~3,486 TF
TF REMAINING: ~2,322 TF
BRIDGE PROGRESS: 76% COMPLETED
TRAIL PROGRESS: 80% COMPLETED



UPDATES BY ROADWAY

LOCATION	CONSTRUCTION ACTIVITY	START	FINISH*	% COMPLETE
Surveyor Blvd. to Midway Bridge	Section on hold until Midway Bridge progresses further.	Dec. 19, 2025	Dec. 31, 2026	75%
Midway Bridge	West of Midway complete. Span 10 deck pour is complete. Working on Spans 7-9 in October.	Nov. 3, 2025	Mar. 14, 2027	76%
Midway Bridge to Railroad Crossing at 2354	MSE Wall is complete. Illumination was removed and crews are rough grading the proposed trail alignment.	Jul. 20, 2026	Dec. 31, 2026	25%
Railroad Crossing at 2354 to Addison Rd.	Illumination was removed and crews are rough grading the proposed trail alignment.	Jan. 26, 2026	Dec. 31, 2026	25%
Addison Rd. Intersection (Incl. RR Crossing)	Hike & Bike trail is complete. Minor fence restoration remains.	Jul. 21, 2025	Oct. 30, 2026	99%
Addison Rd. to Quorum Dr.	Hike & Bike trail is complete and ready for final acceptance.	Jun. 9, 2025	Feb. 6, 2026	100%
Quorum Dr. Intersection	Hike & Bike trail is complete and ready for final acceptance.	Sep. 29, 2025	Jun. 30, 2026	100%
Quorum Dr. to Spectrum Dr.	Hike & Bike trail is complete and ready for final acceptance.	Nov. 3, 2025	Jul. 1, 2026	100%
Spectrum Dr. Intersection	Hike & Bike trail is complete and ready for final acceptance.	Jan. 5, 2026	Jul. 1, 2026	100%
Spectrum Dr. to DNT SB	Hike & Bike trail is complete and ready for final acceptance.	Jun. 23, 2025	Feb. 27, 2026	100%

**Finish dates correspond to construction end dates, not dates which the trail will be open to the public.*
