
PAVING THE WAY: EXPLORE THE NEW

CBR TRAIL

CBR Trail construction is ongoing in the City of Dallas. The following is an update of construction work performed during the month of September 2026.



CITY OF **DALLAS**

COTTON BELT REGIONAL TRAIL *(CBR TRAIL)*


CONSTRUCTION STATUS NEWSLETTER

PROGRESS PHOTOS
See photos of the trail construction:
https://tinyurl.com/CBRT-Dallas-Sept2026

MONTHLY UPDATES
Stay tuned for upcoming monthly newsletters!

CONTACT US!
Reach out to the project team with questions at:
(214) 585-7308

ACTIVITY
Stay posted with updates by roadway *below!*

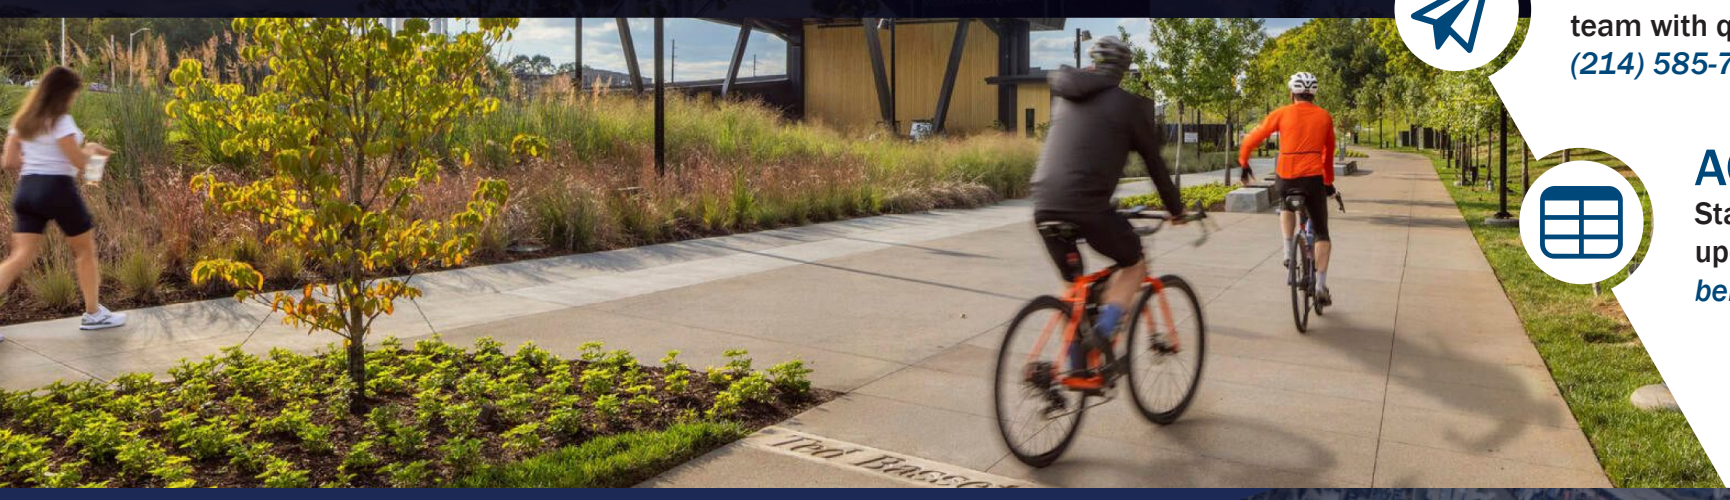

CONSTRUCTION UPDATE MAP

LEGEND
- TRAIL IN PROGRESS
- TRAIL COMPLETE
- PHASE 1 HBT
- CITY OF DALLAS FUTURE TRAIL

BRIDGE 27P:
MCKAMY BRANCH
WORK DATES:
05/14/25 - 08/31/26

DALLAS (3.4 MILES)
WORK DATES: 05/14/25 - 02/24/27
TOTAL FEET (TF): 17,952 TF
TF INSTALLED: ~12,202 TF
TF REMAINING: ~5,750 TF
BRIDGE PROGRESS: 100% COMPLETED
TRAIL PROGRESS: 68% COMPLETED

UPDATES BY ROADWAY

LOCATION	CONSTRUCTION ACTIVITY	START	FINISH*	% COMPLETE
DNT SB Frontage Intersection	Ramps, trail and traffic signals are complete. Awaiting Oncor cutover.	Sep. 29, 2025	Oct. 30, 2026	99%
DNT NB Frontage Intersection	Ramps, trail and traffic signals are complete. Awaiting Oncor cutover.	Oct. 1, 2025	Oct. 30, 2026	99%
DNT NB to Knoll Trail Dr.	Trail and PR11 handrail is complete. Final cleanup and vegetation remain.	Jun. 23, 2025	Oct. 30, 2026	99%
Knoll Trail Dr. to White Rock Creek Bridge	Work by others is nearing completion. Trail scope to restart in October.	Aug. 7, 2025	Dec. 31, 2026	75%
White Rock Creek Bridge to Preston Rd.	Trail construction is underway and will continue through October.	Nov. 10, 2025	Dec. 31, 2026	55%
Preston Rd. to Davenport Rd. West	Trail construction is complete. Final cleanup and vegetation remains.	Aug. 4, 2025	Dec. 31, 2026	95%
Davenport Rd. West Intersection (Incl. RR Crossing)	No work.	Dec. 1, 2026	Dec. 31, 2026	5%
McKamy Bridge	Bridge and Trail construction to crossings is complete. Final clean-up remains.	May 14, 2025	Aug. 31, 2026	100%
Campbell Rd. Intersection	No work.	Nov. 2, 2026	Dec. 7, 2026	0%
Campbell Rd. to Davenport Rd. East	Trail construction is complete. Final cleanup and vegetation remains.	Sep. 17, 2025	Oct. 27, 2026	95%
Hillcrest Rd. Bridge to McCallum Blvd.	Trail and drainage is complete, connection to McCallum remains.	Sep. 15, 2025	Dec. 31, 2026	80%
McCallum Blvd. Intersection	No work.	Apr. 14, 2026	Dec. 31, 2026	5%
McCallum Blvd. to Meandering Way	Sidewalk walls and trail construction are complete. Handrail installation and site restoration remains.	Sep. 17, 2025	Dec. 31, 2026	95%
Meandering Way Intersection	No work.	Nov. 2, 2026	Nov. 30, 2026	0%
Meandering Way to Dickerson St.	Preston Ridge Trail redesign is complete. AWC plans to complete in November.	Aug. 25, 2025	Nov. 30, 2026	80%
Dickerson St. Intersection	No work.	Dec. 1, 2026	Dec. 31, 2026	0%
Dickerson St. to Coit Rd.	Trail rough grading has begun and trail pavement construction to begin in October.	Oct. 6, 2025	Jan. 29, 2027	30%
Coit Rd. to Waterview Pkwy.	Trail construction is complete. Connection to Coit will complete in October.	Nov. 26, 2025	Dec. 31, 2026	98%

**Finish dates correspond to construction end dates, not dates which the trail will be open to the public.*
