
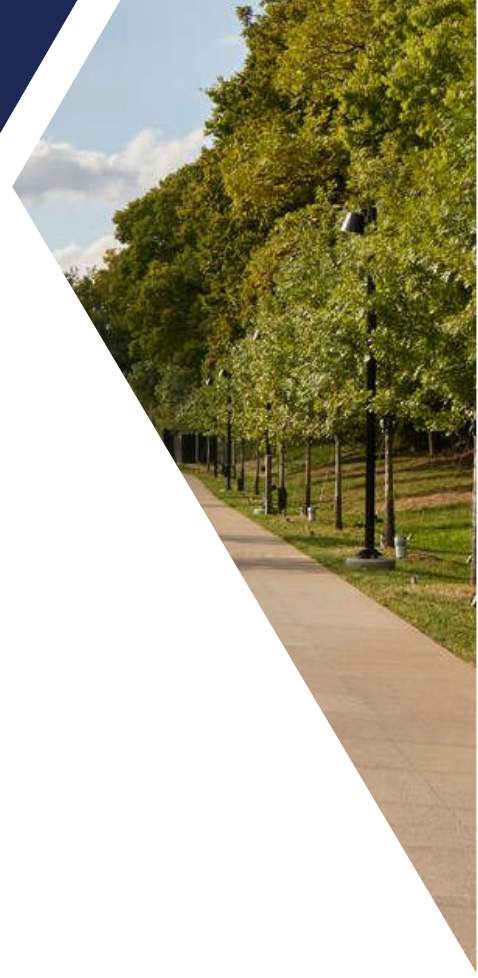


PAVING THE WAY: EXPLORE THE NEW

CBR TRAIL

CBR Trail construction is ongoing in the City of Plano.
The following is an update of construction work performed during the month of September 2026.



CITY OF **PLANO**

COTTON BELT REGIONAL TRAIL *(CBR TRAIL)*


CONSTRUCTION STATUS NEWSLETTER

PROGRESS PHOTOS
See photos of the trail construction:
https://tinyurl.com/CBRT-Plano-Sept2026

MONTHLY UPDATES
Stay tuned for upcoming monthly newsletters!

CONTACT US!
Reach out to the project team with questions at:
(214) 585-7308

ACTIVITY
Stay posted with updates by roadway *below!*

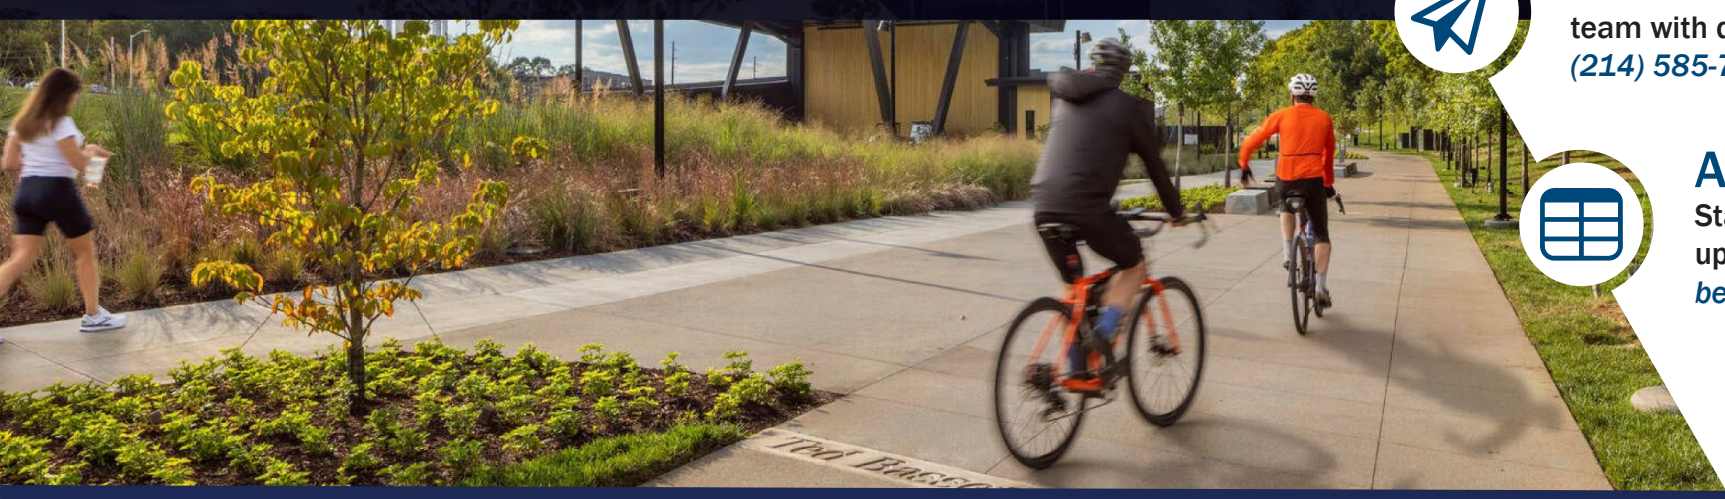

CONSTRUCTION UPDATE MAP

PLANO (3.2 MILES)
WORK DATES: 06/09/25 - 01/21/27
TOTAL FEET (TF): 16,896 TF
TF INSTALLED: ~12,805 TF
TF REMAINING: ~4,091 TF
TRAIL PROGRESS: 63% COMPLETED

LEGEND
- TRAIL IN PROGRESS
- TRAIL COMPLETE
- PHASE 1 HBT

UPDATES BY ROADWAY

LOCATION	CONSTRUCTION ACTIVITY	START	FINISH*	% COMPLETE
PGBT WB Frontage Rd. Intersection	Activation of traffic signal and installation of Luminare poles remain.	Jan. 14, 2026	Dec. 18, 2026	95%
K Ave. Intersection	Activation of traffic signal and installation of Luminare poles remain.	Jan. 19, 2026	Dec. 18, 2026	95%
Municipal Ave Intersection	Ramp and trail complete. Activation of traffic signal remains.	Jan. 22, 2026	Dec. 18, 2026	99%
Municipal Ave to N Ave.	Trail and fence is complete.	Jun. 18, 2026	Sep. 27, 2026	100%
N Ave. to Jupiter Rd. Bridge	Trail construction is complete. Fencing is being installed. Final grading and cleanup remains.	Jun. 9, 2025	Oct. 30, 2026	90%
Jupiter Rd. Bridge to Shiloh Rd.	Trail pavement construction to begin in October.	Jan. 23, 2026	Feb. 23, 2027	60%
Shiloh Rd. Intersection	Traffic signal work is ongoing.	Feb. 3, 2027	Mar. 15, 2027	40%

**Finish dates correspond to construction end dates, not dates which the trail will be open to the public.*
