
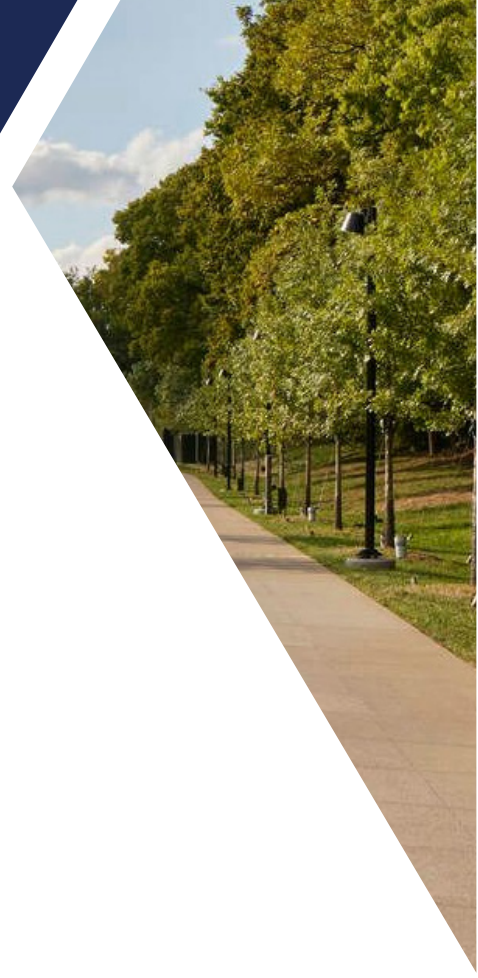


PAVING THE WAY: EXPLORE THE NEW

CBR TRAIL

CBR Trail construction is ongoing in the City of Richardson. The following is an update of construction work performed during the month of September 2026.



CITY OF **RICHARDSON**

COTTON BELT REGIONAL TRAIL *(CBR TRAIL)*


CONSTRUCTION STATUS NEWSLETTER

PROGRESS PHOTOS
See photos of the trail construction:
https://tinyurl.com/CBRT-Richardson-Sept2026

MONTHLY UPDATES
Stay tuned for upcoming monthly newsletters!

CONTACT US!
Reach out to the project team with questions at:
(214) 585-7308

ACTIVITY
Stay posted with updates by roadway *below!*

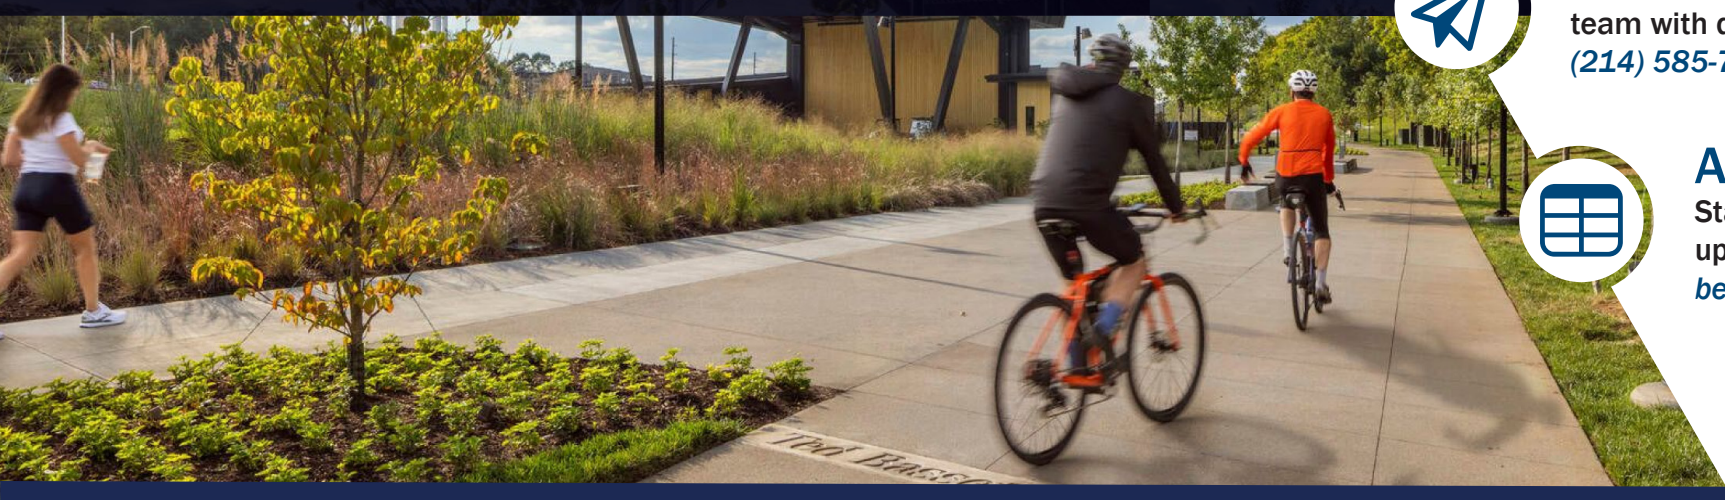

CONSTRUCTION UPDATE MAP

BRIDGE 34P: SPRING CREEK WORK DATES: 06/09/25 - 10/30/26

RICHARDSON (2.8 MILES)
WORK DATES: 05/14/25 - 08/31/27
TOTAL FEET (TF): 14,784 TF
TF INSTALLED: ~8,741 TF
TF REMAINING: ~6,043 TF
BRIDGE PROGRESS: 66% COMPLETED
TRAIL PROGRESS: 68% COMPLETED

BRIDGE 33AP: CUSTER ROAD
WORK DATES: 05/15/25 - 08/31/27

LEGEND
- TRAIL IN PROGRESS
- TRAIL COMPLETE
- CITY OF RICHARDSON FUTURE TRAIL

UPDATES BY ROADWAY

LOCATION	CONSTRUCTION ACTIVITY	START	FINISH*	% COMPLETE
Waterview Pkwy Intersection	Crossing work to begin once trail paving between Coit and Waterview is complete. Traffic signal installation foundation ongoing.	Mar. 25, 2026	Nov. 27, 2026	30%
Waterview Pkwy. to Rutford Rd.	Trail, fencing, and final clean-up is complete.	Sep. 22, 2025	Apr. 30, 2026	100%
Rutford Rd. Intersection	Trail and roadway striping are complete.	Feb. 2, 2026	Aug. 31, 2026	100%
Rutford Rd. to Existing UTD Trail	Trail, fencing, and final clean-up is complete.	Nov. 19, 2025	Sep. 25, 2026	100%
Existing UTD Trail to East of Trestle Bridge	Trail under the KCS Bridge is in design. No work expected until that is complete.	Mar. 2, 2026	Jan. 29, 2027	35%
East of Trestle Bridge to Synergy/Renner Intersection	Trail is 100% complete. Stamped concrete and stone veneer to be constructed in next few weeks. Phase 2 median work remains and will begin once the traffic signal is ready for activation.	Nov. 3, 2025	Dec. 31, 2026	90%
Synergy Park Blvd. / Point North Park Driveway Intersection	Traffic signal activation remains. Phase 2 median work remains and will begin once the traffic signal is activated.	Dec. 1, 2025	Oct. 30, 2026	95%
Synergy Park Blvd. / W. Renner Rd. Intersection	Signal poles have been erected. Trail has been installed north of Renner Rd. Phase 2 median work remains and will begin once the traffic signal is activated.	Jan. 19, 2026	Oct. 30, 2026	90%
W. Renner Rd. / Greenside Drive Intersection	Trail connections and median are complete. Stamped concrete, striping and signage remain.	Jan. 19, 2026	Oct. 30, 2026	90%
South of Greenside Dr.	Trail to the bus stop is complete. Connection under Renner Bridge to has begun.	Mar. 6, 2026	Dec. 18, 2026	60%
W. Renner Rd. to Custer Rd. Bridge	Drainage complete. Installation of RW3310 completed. Crews currently grading for trail.	Apr. 8, 2026	Jan. 6, 2027	50%
Custer Rd. Bridge	Drilled shaft installation continues through mid-October. Bridge substructure construction began with columns and caps being erected. Crashwalls construction begins in October.	Mar. 30, 2026	Jul. 30, 2027	40%
Custer Rd. Bridge to Alma Rd.	Arch culverts are complete and backfilled. Trail rough grading on-going	Apr. 15, 2026	Feb. 19, 2027	50%
Alma Rd. Intersection	No work.	Dec. 1, 2026	Jan. 29, 2027	0%
Spring Creek Bridge	Bridge and railing is complete. Signage remains.	Jun. 9, 2025	Oct. 30, 2026	99%
Spring Creek Bridge to Red Moon Way	Trail construction is complete. Final clean up and vegetation remains.	Jun. 9, 2025	Oct. 30, 2026	99%
West City Line Dr. Intersection	Routh and City Line intersections are poured out. Fencing installation complete.	Sep. 29, 2025	Jul. 24, 2026	100%
West City Line Dr. to PGBT EB Frontage	Trail construction is complete.	Jul. 7, 2025	Sep. 25, 2026	100%
PGBT EB Frontage / Routh East Dr. Intersection	Trail construction is complete. Signal activation remains.	Sep. 10, 2025	Oct. 30, 2026	99%
PGBT EB Frontage to PGBT WB Frontage	Scope is 100% complete.	May 14, 2025	May 8, 2026	100%

**Finish dates correspond to construction end dates, not dates which the trail will be open to the public.*
